RAJESHGANESH
ROLL NO 241501161

EXPERIMENT 11

Development to production deployment

Aim

Prepare and verify a controlled release of the library application through the environments supported by the account.

Procedure

1. Confirm environments are available and the release operator has the necessary permissions. Identify development, stage and production. If unavailable, document a design-only release exercise using separate test and production apps without claiming equivalence to managed environments.

2. Prepare release version 1.0 with a change list, schema dependencies, tests, responsible owner, migration steps and recovery plan. Freeze edits during the release review.

3. Publish the development changes to stage using the available environment publishing flow. Review component dependencies, warnings and blocked changes. Do not assume a partial selection includes every required field or function.

4. Configure stage connections and endpoints for test services. Verify connection authorizations, schedules, email routing and portal permissions. Do not assume development credentials or data are promoted automatically.

5. Run T01 to T12 and the access and integration tests in stage. Resolve failures. Record reviewer approval and a maintenance window appropriate to the institution.

6. Back up the current production state using supported tools and verify what is included. Prepare any required data migration separately from application-definition publishing; test it on representative data.

Implementation and verification

7. Publish the approved stage version to production. Verify production connection ownership, environment-specific values, schedule activation and permissions. Run a limited smoke test with identifiable test data and approved recipients.

8. Observe logs and failed queues after release. On a critical failure, stop affected writes, preserve evidence and follow the tested recovery plan. Do not assume one-click rollback restores both schema and data safely.

Release gate	Acceptance evidence
Functional	Issue, return, date boundary and invalid-input tests pass.
Security	All role tests pass; no public sensitive report.
Integration	Correct environment and CRM organization; failures visible.
Data	Backup verified; migration counts and lookups reconcile.
Operations	Owner, recovery steps and monitoring are documented.

Evidence


E11: release notes, stage test log, dependency review, approval record, backup reference, production smoke-test record and recovery rehearsal. If production access is not authorized, stop at the release-ready package and mark publishing Not run.

Implementation and interpretation

Publishing an application definition and migrating operational data are separate concerns. Review supported environment behavior, credentials, schedules and dependent components. Verify the recovery path before the release, including what cannot be restored automatically.

Application images and explanation

Illustrative process diagram

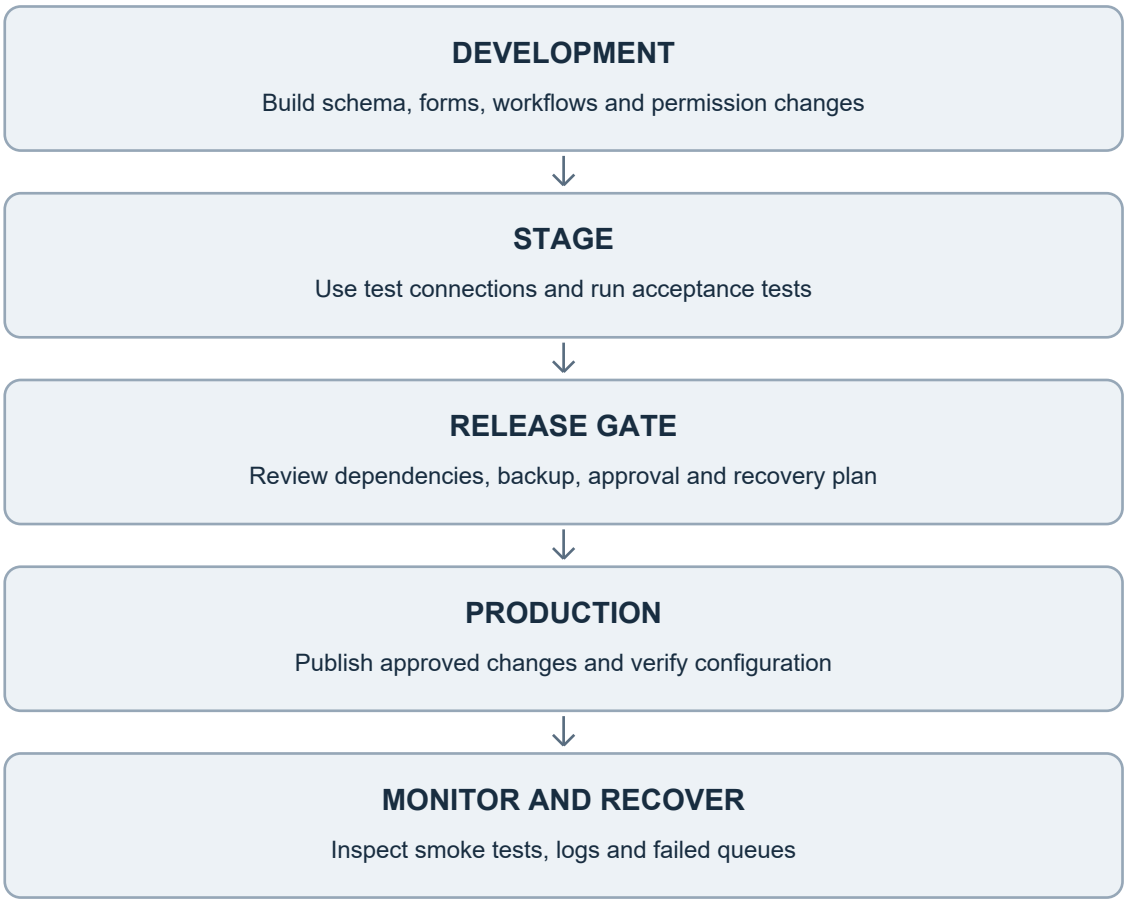

Generated explanatory diagram. It is not a screenshot of an executed workflow.

Publishing an application definition and migrating operational data are separate concerns. Review supported environment behavior, credentials, schedules and dependent components. Verify the recovery path before the release, including what cannot be restored automatically.

Result

Expected result and verification criteria. The release can be accepted only when the documented gates and smoke tests pass. Otherwise the record identifies the blocked gate and retained recovery path; it does not claim production deployment occurred.
